


MANDATORY PRE-CONSTRUCTION INSPECTION:
 FAILURE TO OBTAIN CITY INSPECTION PRIOR TO DRIVEWAY CONSTRUCTION WILL RESULT IN \$85 FINE AND CORRECTION OF ALL WORK DEEMED OUT OF COMPLIANCE WITH PERMIT.
 CALL CITY ENGINEERING DEPARTMENT TO SCHEDULE REQUIRED INSPECTION: 360-537-3215.

- DIMENSION LIST (FILL IN BLANK DIMENSIONS):**
- D 6" RESIDENTIAL, 8" MINIMUM COMMERCIAL
 - D2 2" RESIDENTIAL, 4" MINIMUM COMMERCIAL
 - L1 _____ (EXISTING PLANTER STRIP WIDTH)
 - L2 _____ (EXISTING SIDEWALK WIDTH)
 - W1* _____ (PROPOSED DRIVEWAY WIDTH)
 - S1 1V:12H MAXIMUM SLOPE
 - S2** 1% MINIMUM SLOPE, 2% MAXIMUM SLOPE
 - S3 1V:12H MAXIMUM SLOPE
- * MINIMUM WIDTH 10', MAXIMUM WIDTH 30'
- ** NEW SIDEWALKS WITH CROSS-SLOPE GREATER THAN 2% SHALL BE REMOVED AND REBUILT AT APPLICANT'S EXPENSE.

NOTES:

1. CONCRETE SIDEWALK SHALL BE CLASS 4000 PER WSDOT STANDARD SPECIFICATIONS.
2. ROUND ALL CONCRETE EDGES 1/2".
3. WORK SHALL CONFORM WITH WSDOT STANDARD SPECIFICATIONS.
4. ALL CUTS SHALL BE CLEAN AND STRAIGHT BY USE OF A SAW CUTTING TOOL.
5. PROPOSED DRIVEWAY SHALL BE ASPHALT PAVEMENT FROM EDGE OF THE ROADWAY TO THE EXISTING SIDEWALK. THE ASPHALT DRIVEWAY SHALL BE CONSIDERED TEMPORARY AND SUBJECT TO REMOVAL AND REPLACEMENT AT THE EXPENSE OF THE ABUTTING PROPERTY OWNER AT SUCH TIME AS STANDARD CURBS AND GUTTERS ARE CONSTRUCTED.

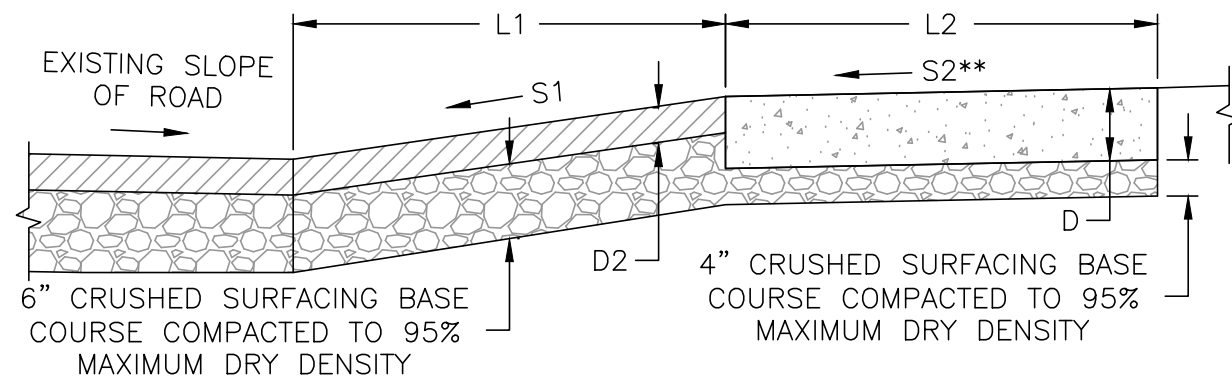

SECTION A-A

TO BE COMPLETED BY CITY		DRIVEWAY PERMIT STANDARD DETAIL FORM	
DRIVEWAY PERMIT NO. _____		DRIVEWAY TYPE IV: SIDEWALK, PLANTER STRIP & NO CURB	
APPROVED BY: _____		CITY OF ABERDEEN ENGINEERING DEPT.	
DATE APPROVED: _____		200 E MARKET ST. ABERDEEN, WA 98520	DRAWING IS NOT TO SCALE DRAWING VERSION 20170630

